

KEY

- # - Sidewalk project (circle)
- # - Bikeway project (square)

### COMPLETED PROJECTS

- 1 Sidewalk:** A new sidewalk was constructed on Murfreesboro Pike from Nashboro Blvd. to Nashboro Village Entrance. This project is complete, with construction finished September 2023.
- 2 Sidewalk:** A new sidewalk was constructed on Edge O Lake Drive from Bell Rd. to Deerpath Dr. This project is complete, with construction finished October 2023.

### PROJECTS IN CONSTRUCTION

- 1 Bikeway:** A shared bikeway is being constructed on Priest Lake Drive from Anderson Rd. to Anderson Rd. This project's completion date is weather dependent. Construction began February 2023 and is estimated to end early 2024.
- 2 Bikeway:** A protected bike lane is being constructed on Edge O Lake Drive from Murfreesboro Pk. to Bell Rd. This project's completion date is weather dependent. Construction began November 2023 and is estimated to end early 2024.


### PROJECTS IN DESIGN

- 3 Sidewalk:** A new sidewalk is in the design phase on Murfreesboro Pike from Rural Hill Rd. to Lake Villa Dr. This project is currently in the plan/design phase with an estimated construction start date in April 2024.

### PLANNED PROJECTS


- 4 Sidewalk:** A new sidewalk is being planned on Murfreesboro Pike from Una Antioch Pk. to British Woods Dr. The planning team is currently acquiring right-of-way for this project.
- 5 Sidewalk:** A new sidewalk is being planned on Hamilton Church Road from Murfreesboro Pk. to East of Hamilton Creek Apartments. This project is currently in the data collection phase.
- 3 Bikeway:** A bike lane is being planned on Anderson Road from Bell Rd. to Smith Springs Rd. This project is currently in the plan/design phase.

 **Interactive Sidewalk Tracker:** <https://cfms.nashville.gov/Sidewalks/Home/InteractiveMap>

 **Interactive Bikeway Tracker:** <https://cfms.nashville.gov/Bikeways/Home/InteractiveMap>

 **hubNashville:** [https://hub.nashville.gov/s/request-type/aOut00000000IICHAA0/streets-roadssidewalks?language=en\\_US](https://hub.nashville.gov/s/request-type/aOut00000000IICHAA0/streets-roadssidewalks?language=en_US)

# Sidewalk and Bikeway Projects

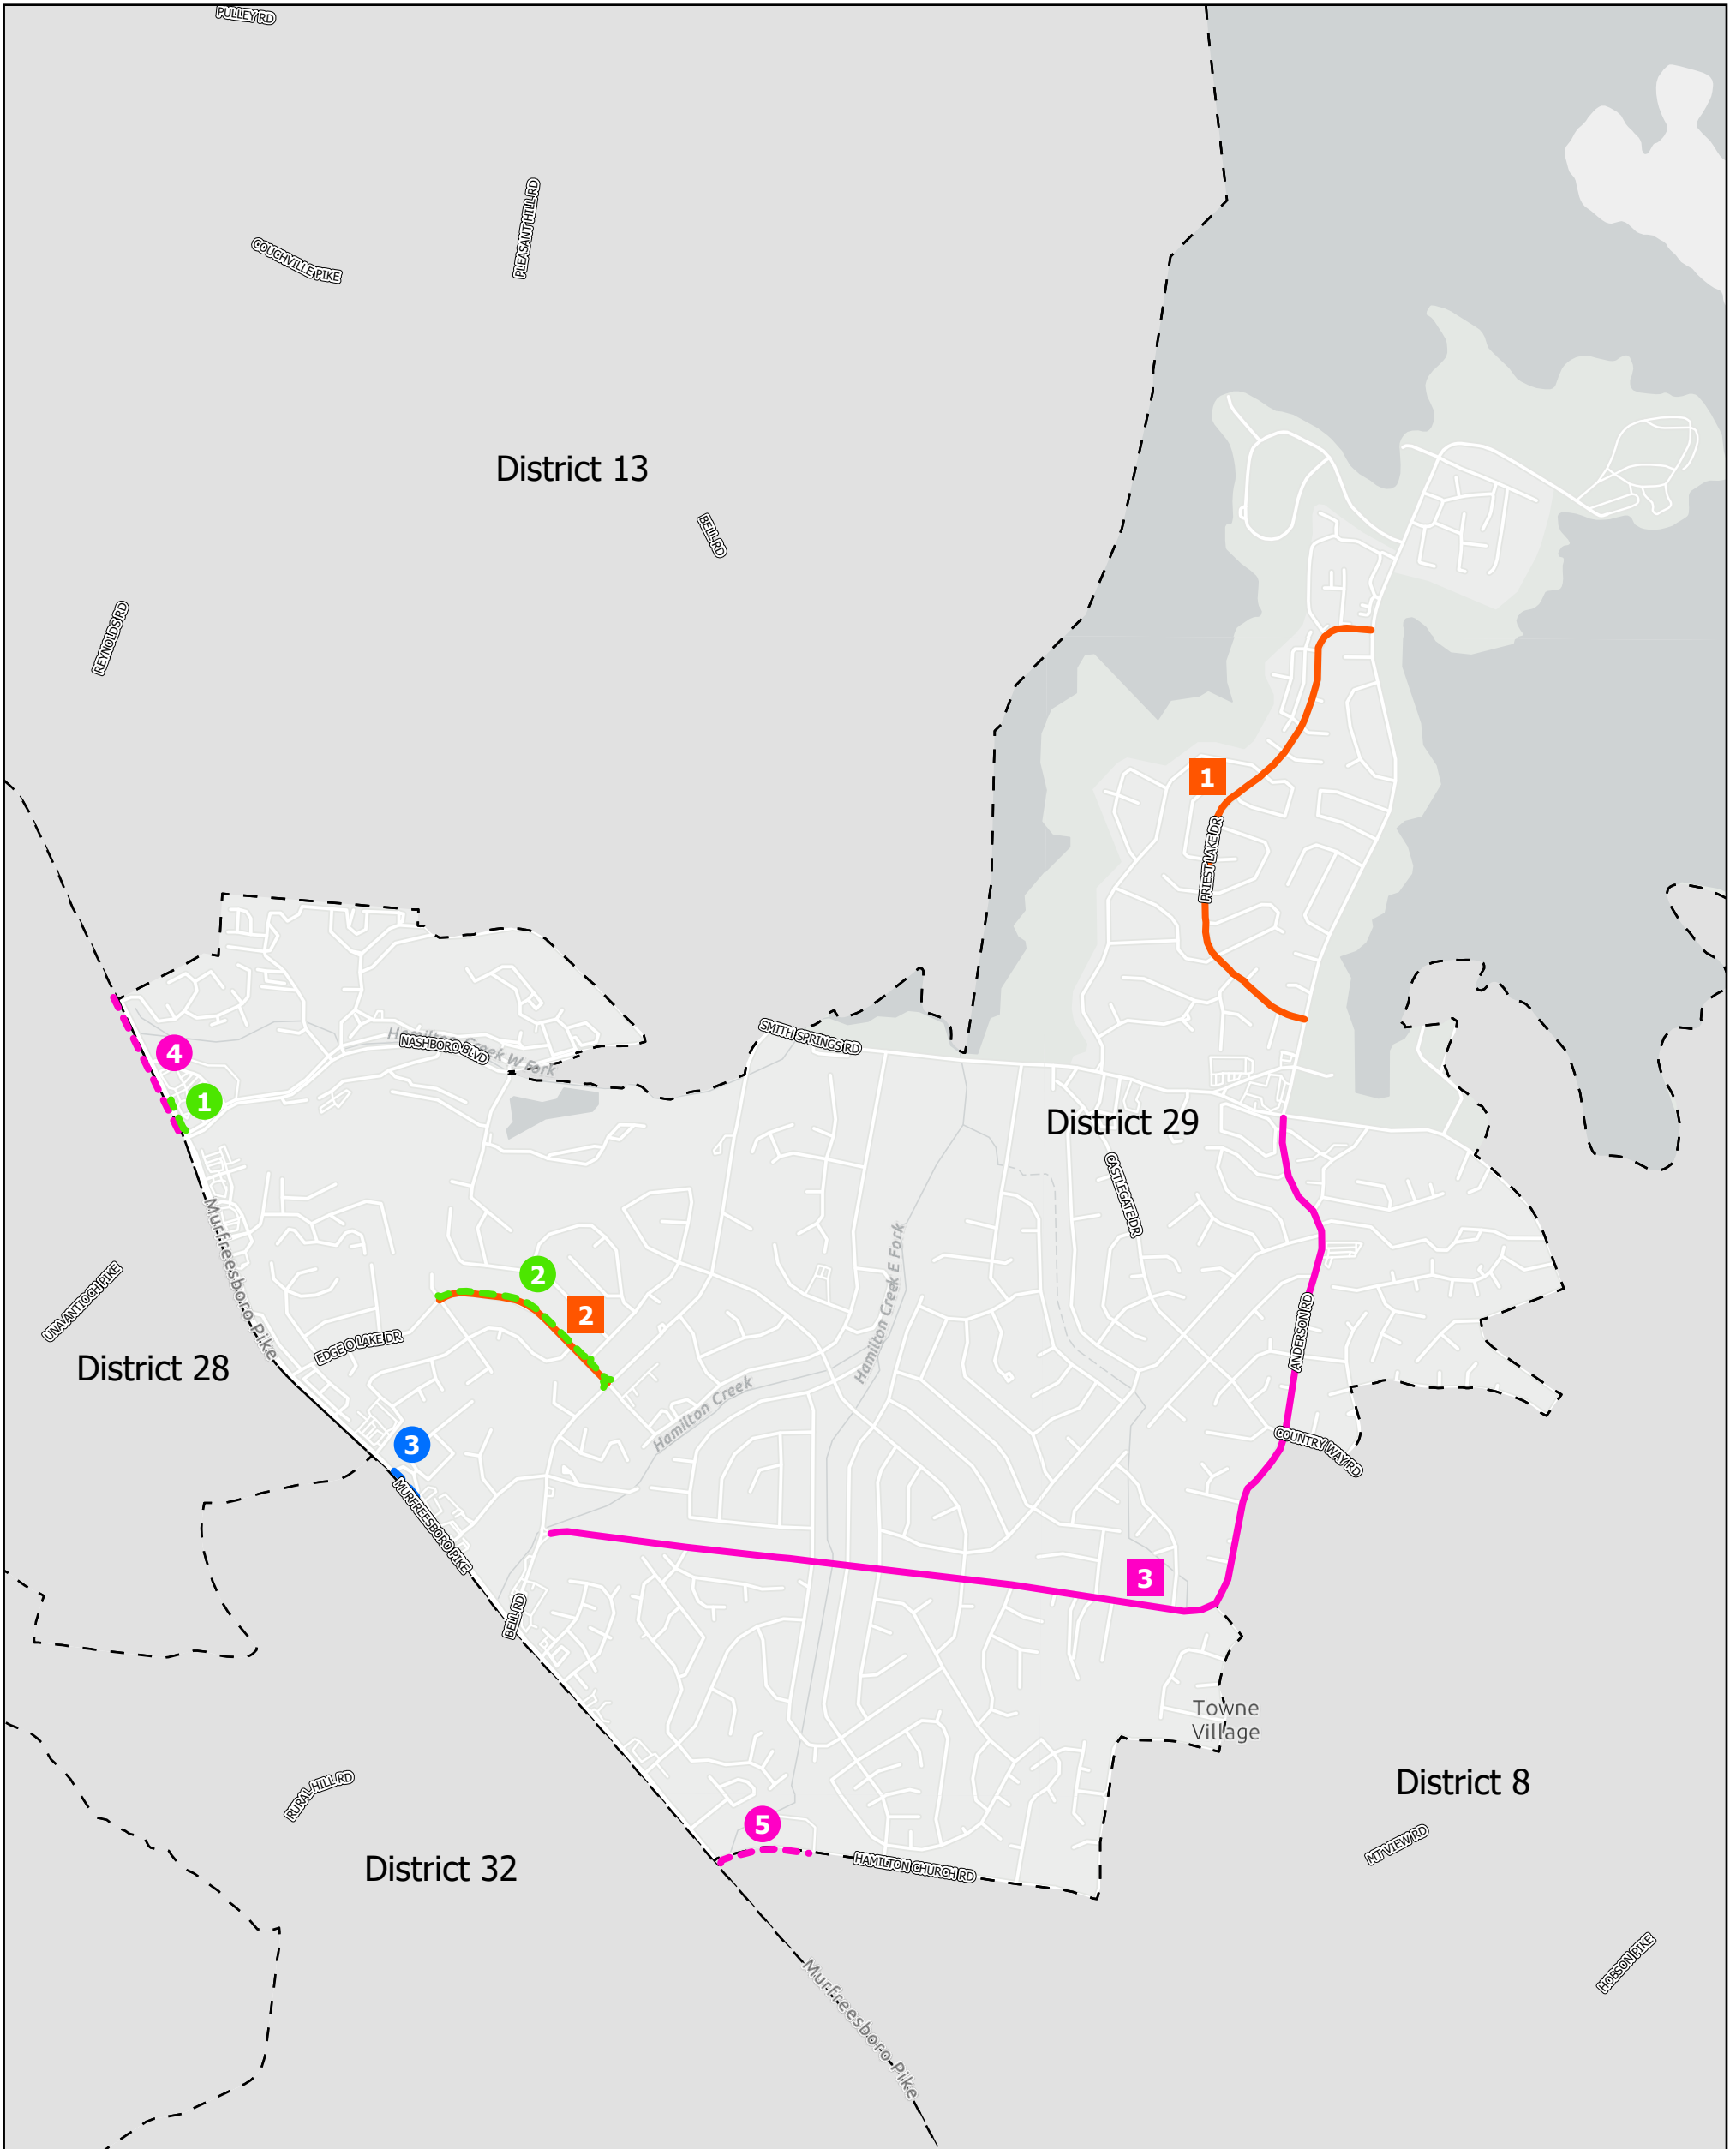

0 0.5 1 Miles

## Legend

### Sidewalk Projects

- Complete
- Construction
- Design
- Planning

### Bikeway Projects

- Complete
- Construction
- Design
- Planning

## Council District 29

**NDOT**

